



Partial Rebuild Bulletin

Issue 3

“Be very careful, then, how you live – not as unwise but as wise, making the most of every opportunity.” 5 Ephesians 15 - 16

WB 16 October 2023

Groundworks continued to prepare for the installation of the temporary block. Surveys were completed to assess how to connect services to the block.

WB 30 October 2023

Site offices and facilities for the construction team are now in position on the overflow car park.


This fortnightly bulletin will provide you with a progress update for our partial rebuild of St Peter's Collegiate Academy. It will feature any adjustments to the proposed timeline, what has been undertaken over the preceding two weeks and some photos to show the current state of the rebuild.

The area for the temporary block is still undergoing significant groundworks to install drainage and prepare for a connection of services. To support this work there has been an increase in the number of construction staff working on the extended site. In order to accommodate the construction staff new offices and workspaces have been installed on the overflow car park.



In addition to the preparation of the site for the temporary block work has also begun on the temporary car park which will be used by staff and visitors. This is critical work because the main car park will be used to locate a temporary reception and offices from Easter 2024 onwards.

Our next meeting with Keir is scheduled for the week beginning Monday, 27 November 2023. Following the conclusion of this meeting I will be able to share our proposed planning for the movement into the temporary block from A block prior to its demolition.

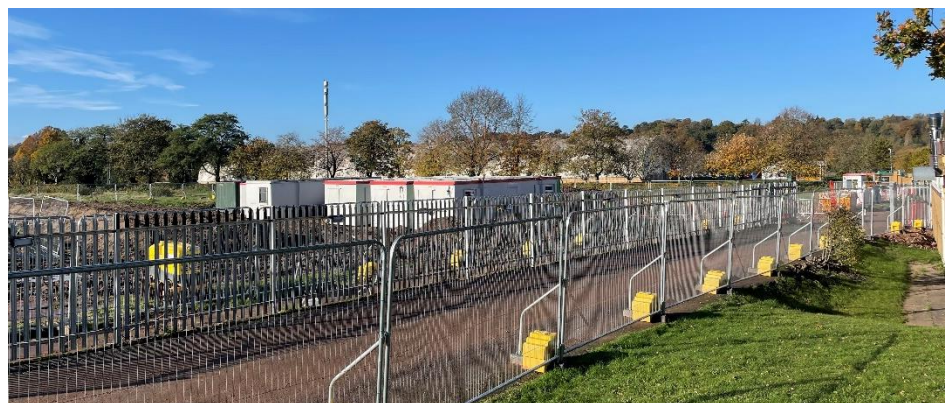

12 January 2026

The new Academy block replacing A-block will be open to pupils.
